


The drawing is based on information contained within the survey carried out by Elciff Consultancy Limited, Arboricultural Consultancy, Wharfedale, Underhill, Giggleswick, North Yorkshire, YO21 2PF, Tel: 01404 887819

This drawing is the copyright of tpm landscape Ltd and cannot be reproduced in any form without the consent of the company. When used scaled dimensions to be checked on site, any discrepancies reported prior to work commencing. P:\2022\71332\01

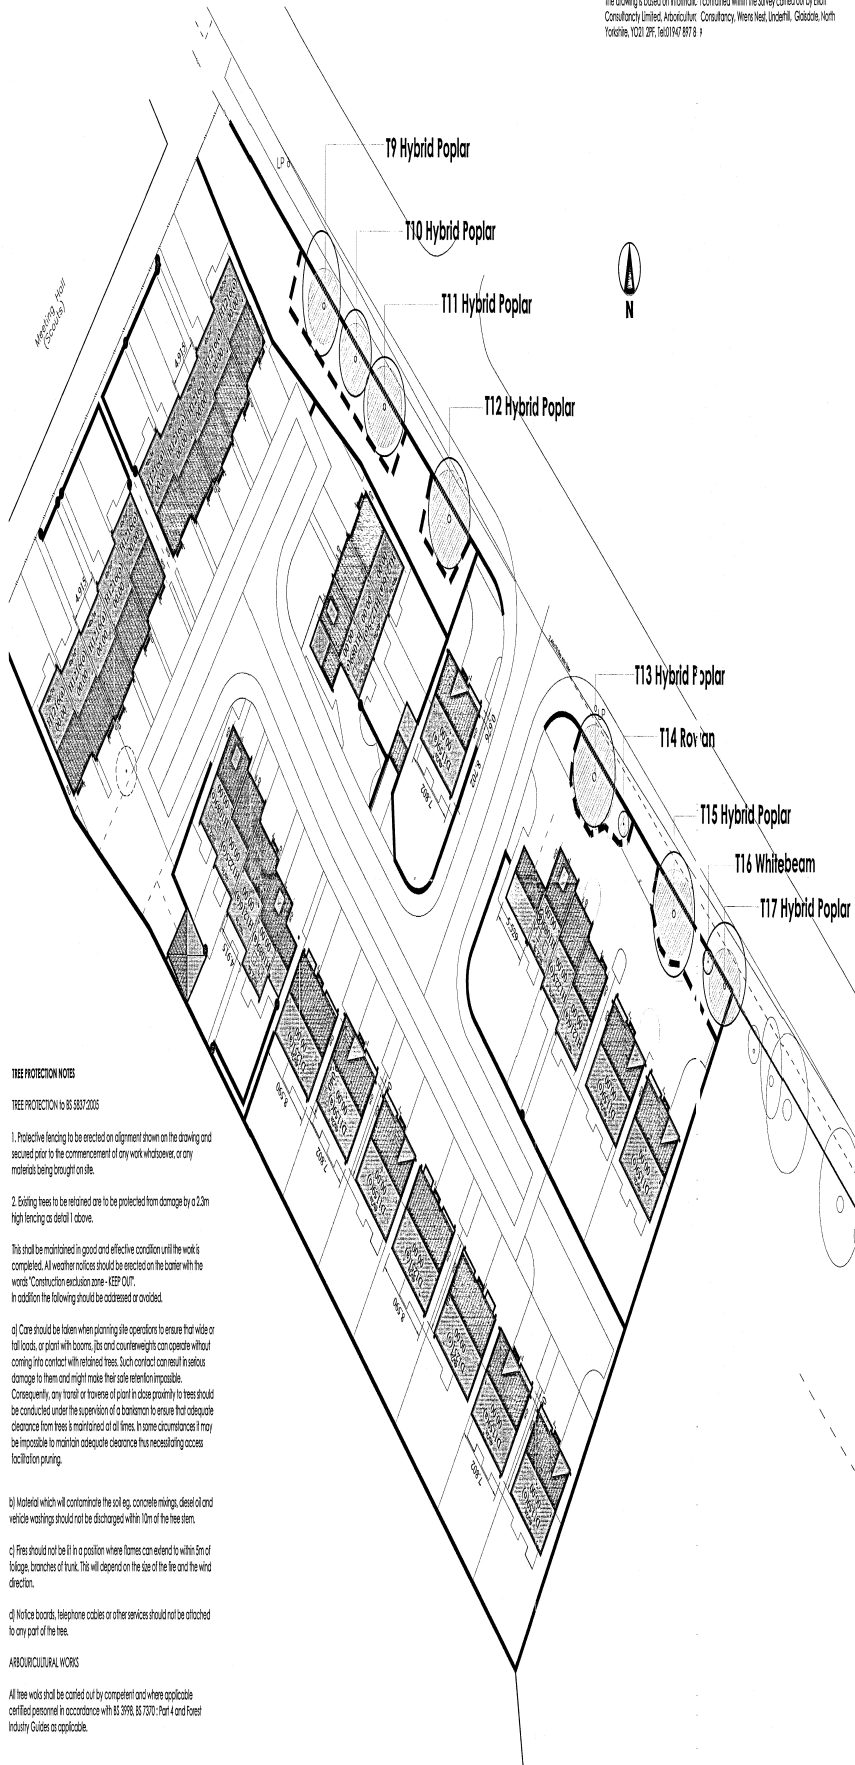

LEGEND

- Existing trees/vegetation to be retained
- Existing trees/vegetation to be removed
- Existing site trees/vegetation
- Proposed Tree Protection fence to be either secured fence or 2.1m high chain checked pole or scaffold pole framework
- Root Protection Area (RPA) as defined in BS:5837

TREE PROTECTION NOTES

TREE PROTECTION to BS:5837:2005

1. Protective fencing to be erected on alignment shown on the drawing and secured prior to the commencement of any work whatsoever, or any material being brought on site.

2. Existing trees to be retained are to be protected from damage by a 2.1m high fencing as detail 1 above.

This shall be maintained in good and effective condition until the work is completed. All weather notices should be erected on the barrier with the words "Construction exclusion zone - KEEP OUT". In addition the following should be addressed or avoided.

a) Care should be taken when planning site operations to ensure that wide or tall loads, or plant with booms, jibs and counterweights can operate without coming into contact with retained trees. Such contact can result in serious damage to them and might make their safe retention impossible. Consequently, any transport or traverse of plant in close proximity to trees should be conducted under the supervision of a bailiwick to ensure that adequate clearance from trees is maintained at all times. In some circumstances it may be impossible to maintain adequate clearance thus necessitating access facilitation piling.

b) Material which will contaminate the soil, eg. concrete mixings, diesel oil and vehicle wastings should not be discharged within 10m of the tree stem.

c) Fires should not be lit in a position where flames can extend to within 5m of foliage, branches or trunk. This will depend on the size of the fire and the wind direction.

d) Notice boards, telephone cables or other services should not be attached to any part of the tree.

ARBOCULTURAL WORKS

All tree works shall be carried out by competent and where applicable certified personnel in accordance with BS:3998, BS:3700, Part 4 and Forest Industry Guides as applicable.

tpm landscape
 chartered landscape architects

07 / 2732 / --

Client: George Wimpsey North Yorkshire Ltd
 Project: Greenwood Road, Billingham

Description: Tree retention and removals

Date: For information
 Date: 1:20 AM
 Job number: 793 01 /

Copyright tpm landscape Ltd
